


Moselle Schedule

Revision: r5

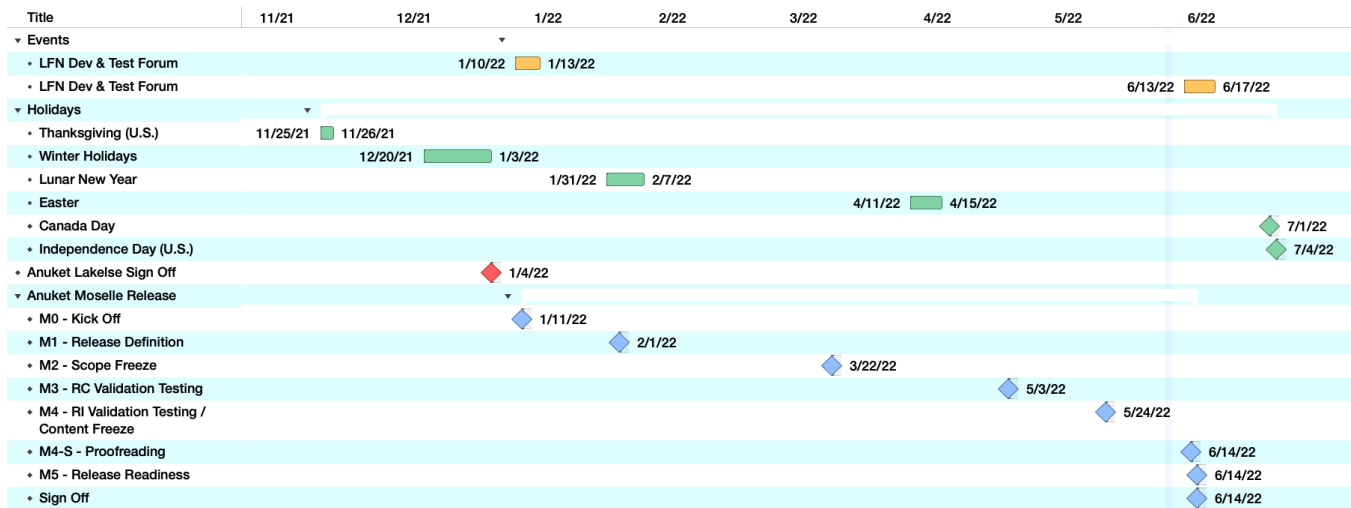

Change Log

Date	Revision	Event / Change	Milestones Affected	Notes
June 21		The TSC approved M4-S, M5, and Sign Off	M4-S, M5, Sign Off	
June 14		TSC deferred M4-S, M5, and Sign Off to June 21	M4-S, M5, Sign Off	
June 7	r5	TSC agreed to push M4-S and M5 out to June 14, concurrent with Sign Off.	M4-S, M5	The TSC agreed that in the future we will combine M5 release readiness with Sign Off, rather than having separate milestones.
May 24	r4	TSC approved M4, contingent upon review of PRs at the next TSC meeting	M4	
Apr 19	r4	TSC approved revised schedule	M3, M4, M4-S	M3 slips two weeks. M4 and M4-S slip one week. Signoff stays the same.
Mar 29	r3	TSC approved change to release process	M3, M4, M4-S	- New milestone added (M4-S) "Specification created" task moved from M3 to M4 "Proofreading" task moved from M4 to M4-S - Dates for existing milestones unchanged
Feb 1	r2	TSC approved M1	M1	
Dec 15	r2	Updated events, and Lakelse Sign Off	None	
Dec 14	r1	Approved by the TSC	all	
Dec 14	r1	second draft	M0, M1	Moved kickoff to Jan 11 and M1 to Feb 1
Nov 1		Initial draft	All	
